



REFIT REPORT

R11

Project Name : M/Y 60 m Grand Rusalina
Project Category : Refit
Start Date : 02.12.2022.
Finish Date : 31.03.2023
Total Duration : 120 days
Publish Date : 31.03.2023.

CONFIDENTIALITY NOTICE

This document contains proprietary technological information. This document is private and confidential to the exclusive use of the individual or entity to whom it is addressed. It may also be legally confidential. Any disclosure, distribution, or other dissemination of this document to any third party is strictly prohibited. If you are not the intended recipient, you may not copy, forward, send or use any part of it. If you are not the intended recipient or the person who is responsible for transmitting it to the intended recipient, please contact the sender by reply e-mail and destroy all copies of the original message and its attachments.

LEGAL NOTICE

Mengi Yay has the right to make any modification on any information given in this manual without prior notice. Sketches, drawings may contain any additional upgrades and some features may be hidden on figures.

CONTENTS

Glossary of Terms	4
Executive Summary	6
Introduction	7
Works In Detail	13
Pending Quotations for Next Refit	351
Refit Certificate	353
Confirmation of Receipt	354

Glossary of Terms

Shipyard Representative	SR
Project Manager	PM
Client Representative	CR
Client	Mr. C
Chief Officer	CO
Chief Engineer	CE
Variation Certificates	VC
Refit Specifications	RS

Executive Summary

This document contains explanatory details for all the work done with certificates and images. Main work items are named *Refit Specification* items, Change Orders or Additional Works are named *Variation Certificates and Refit Specification* or Variation Certificate Items that are cancelled are named Credit Items. There are 29 refit specification items, 36 Variation Certificates and 4 Credit Items requested by the client. Although the original contract was 60 days, with requested variation certificates by the client and an additional 60 days is added to initial delivery date, making the contract 120 days long.

Refit Location : Pendik Marintürk, Istanbul, Turkey

Shipyard Representative : Ramazan Mengi

Project Manager : Sedat Baş

Number of Completed Works : 65

Departments Concerned at MY : Piping and Systems, Interior, Project Management, Business Development, Upholstery, Painting, Insulation, Cleaning, Machinery

All the subcontractors and yard's workers have been managed by the attained Project Manager. Shipyard Representative was also attained to conduct the communication with the Client Representative. Weekly meetings were conducted with the client representative, crew, and project manager to discuss new variation certificates and issues regarding the occurring jobs.

Next Refit

MY is aware that Grand Rusalina will need another refit for painting and for items that have been quoted but CR and Mr. C didn't have enough time to decide in 120 days of refit period. CR has requested a second refit quotation which MY is currently preparing. Further information can be found in *Pending Quotations for Next Refit*.

Current Number of New RS Items: 16

Introduction

This document contains explanatory details for all the work done with certificates and images. Main work items are named *Refit Specification* items, Change Orders or Additional Works are named *Variation Certificates* and Refit Specification or Variation Certificate Items that are cancelled are named Credit Items. There are 29 refit specification items, 36 Variation Certificates and 4 Credit Items requested by the client.

Project Management


Project is managed by Project Manager and overviewed by Shipyard Representative who conducts the communication with the Client Representative. Client Representative manages the approval and rejection of jobs and is responsible for transmitting the request of the Client.

Meeting Procedure


All the meetings took place in the yacht upper deck dining area with at least two members from the crew (Chief Officer, Chief Engineer, Captain, Steward) and progress meeting notes were shared by CR via e-mail.

Works Completed and Accepted Timeline

The work list and delivery deadline are scheduled according to the crew and CR's feasibility, thus any work conflict between crew's ongoing schedule and yard's work occurred. The timeline of the works completed and accepted is below.

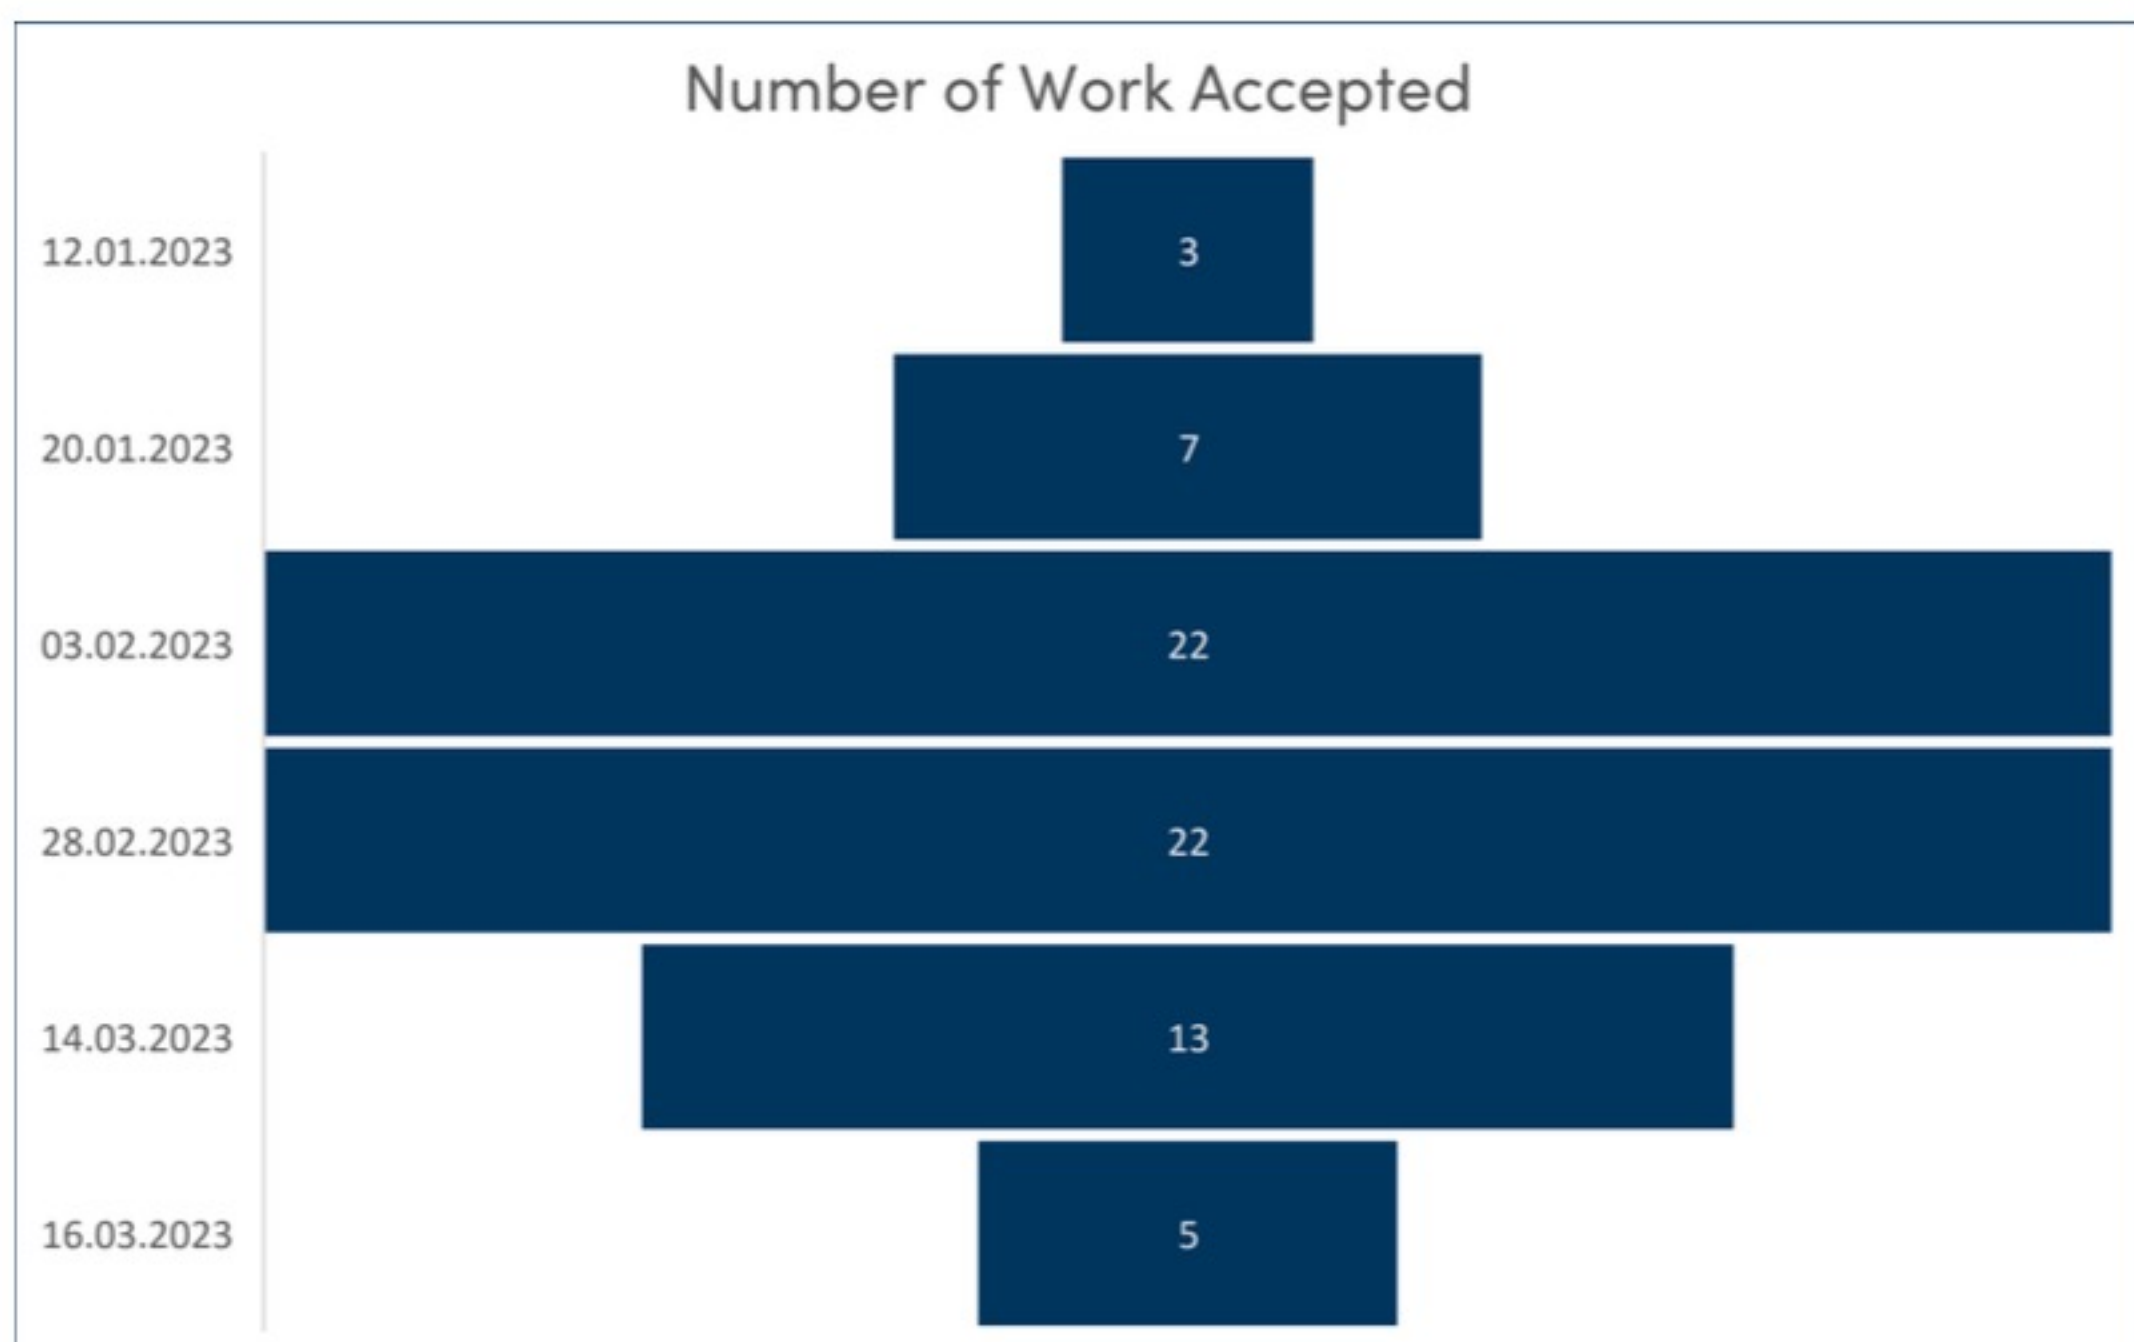

Variation Certificate Approval Protocol

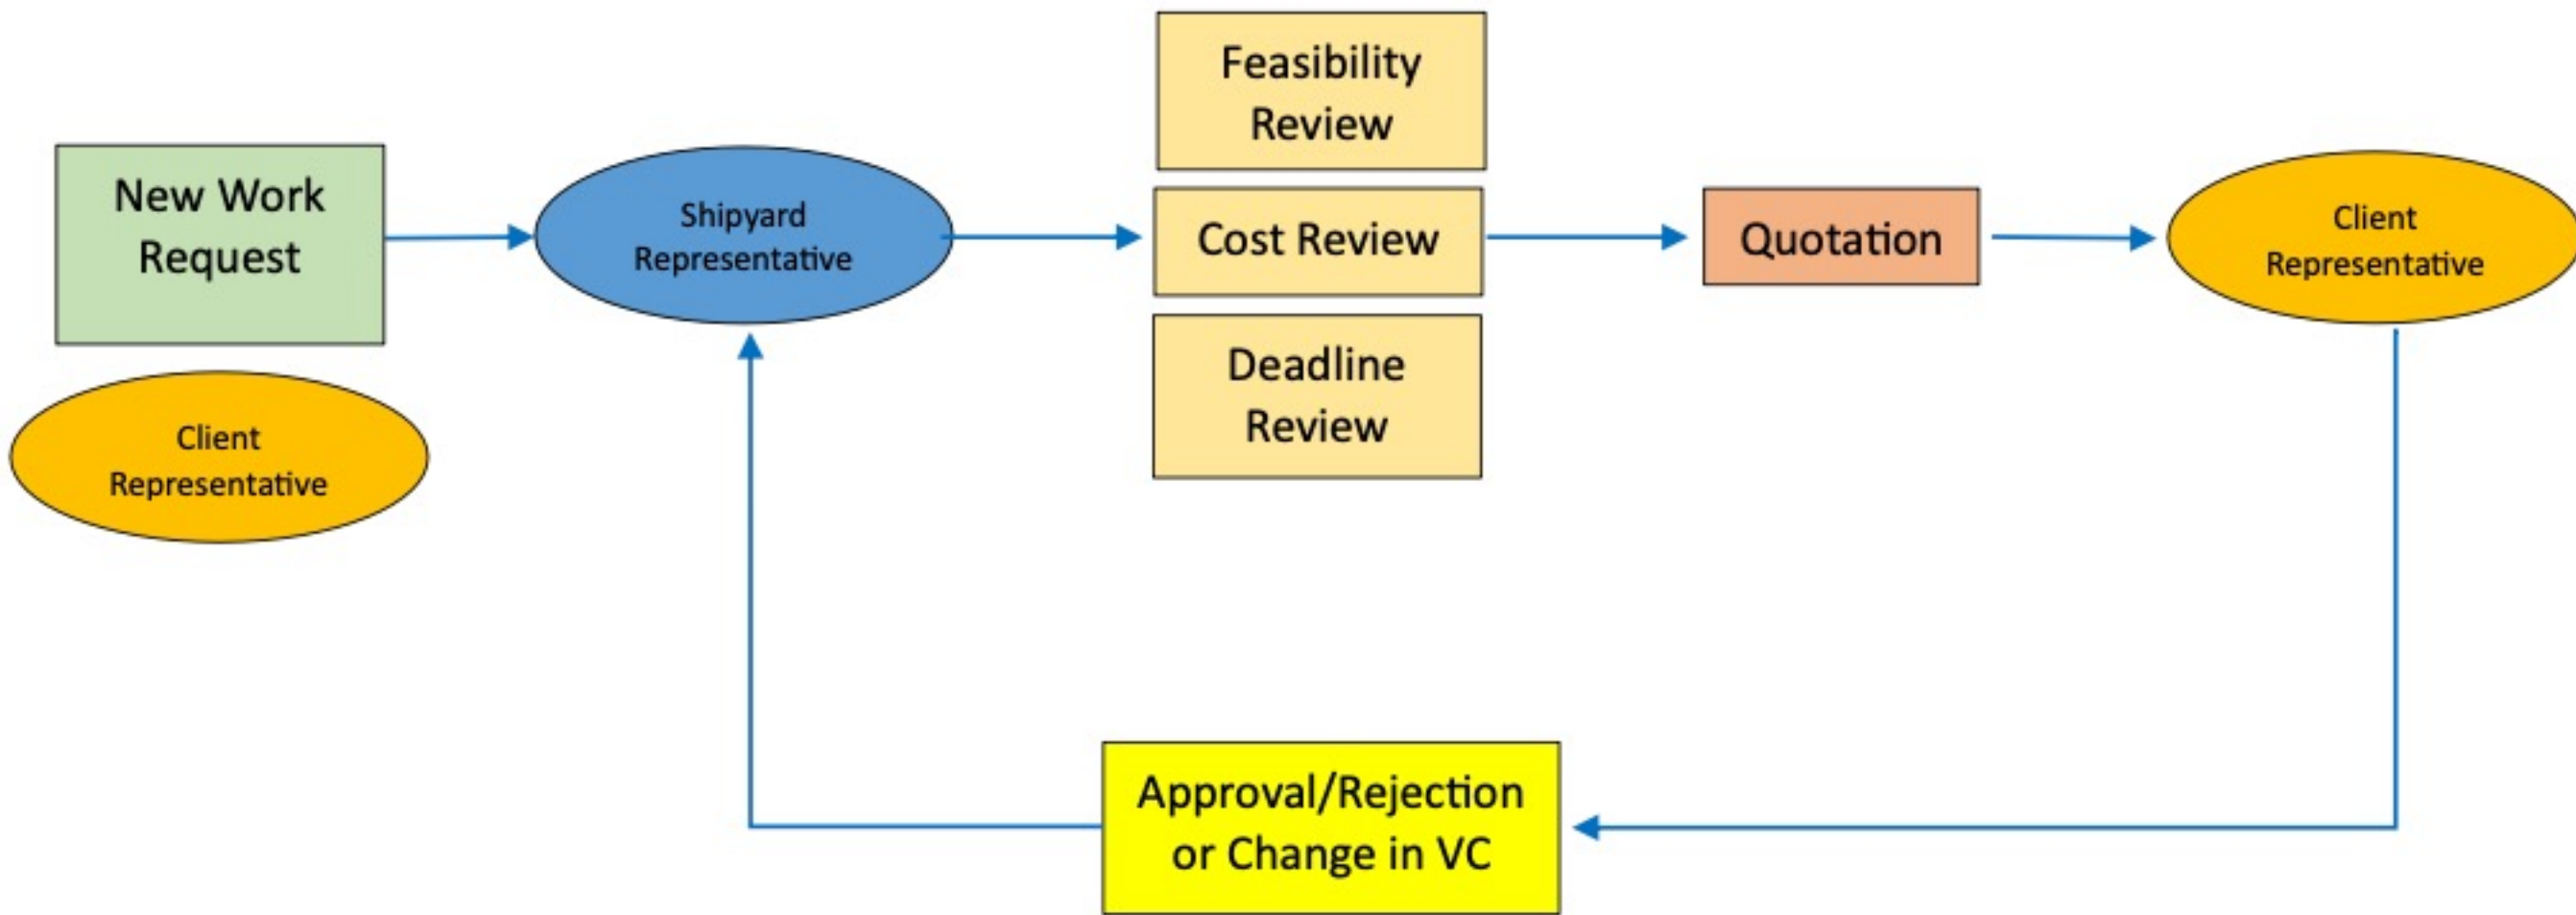

Work Acceptance or Rejection Protocol

